BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Road and Drains at Agrahra Village in Ward NO 05 Byatarayanapura Sub Divison	
2	Estimate Cost	20.00 Lakhs	
3	Administrative Approved No and Date	581/2013-14, Date. 23.12.2013	
4	Technical sanction No. and Date	75/13-14, Date. 23.12.2013	
5	Job Code No. and P Code No.	006-14-000048	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	379/2013-14, Date. 21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	26.05.2014	
12	Actiual Date of Completion	28.07.2014	
13	Delay if any	Nil	

14	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	25.06.2015	
19	MB No. and Page No.	Mb No . 2503 Page No. 250201-07	
20	BR No and Date	207/31.07.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultents and Engineers is verified and Enclosed	
22	Section officer	Sri Chandrakanthraju AE	
23	Sub Division Officer	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
A	Work Quality	Satisfactory	
B	Comments	Work completed as per MB	

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ವಿಭಾಗ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಬೆಂಗಳೂರು-560092.

25/06/15

Y.C. Kalagowda
E.E (Rtd)

Name of Work :- Improvements to Road & Drains at Arrahara village in Ward No-5 Byatarayanapura Sub-division

AE-05

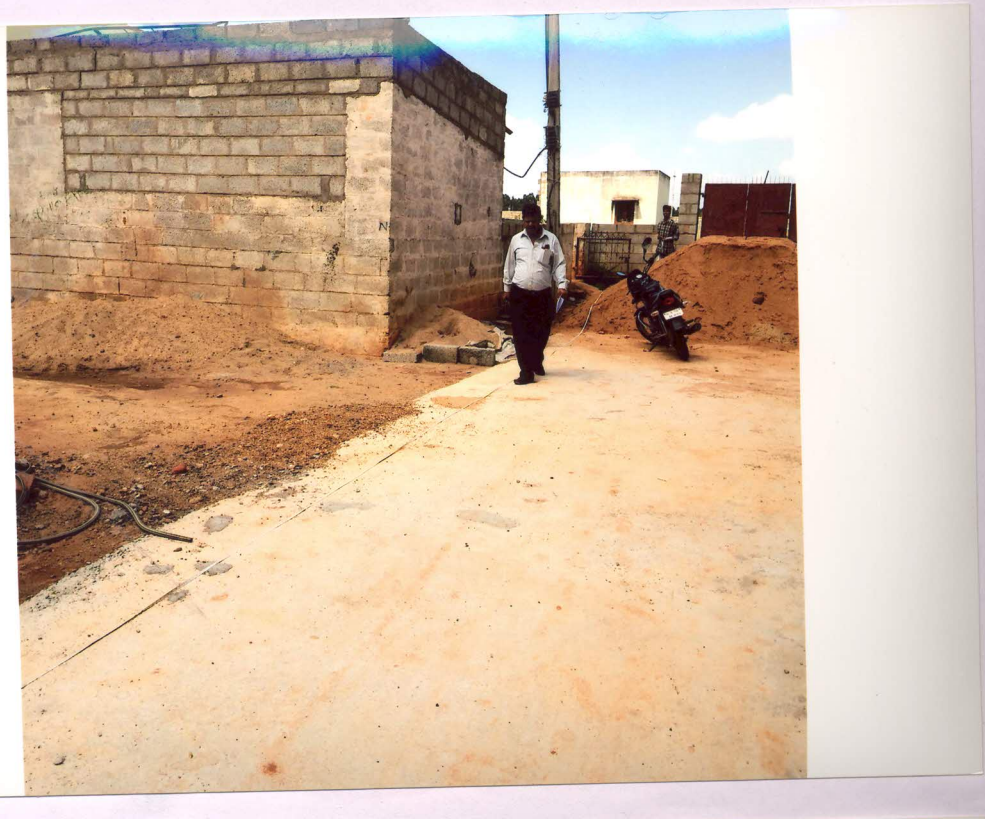

AG-05

dy AE-05
